



CONSTRUCTION PROJECT LOG

Prepared by

Office of Transportation System Management

Last updated on: 10-7-2022

Control Section 3303

TRUNK HIGHWAY: MN47

COUNTY: Kanabec

DISTRICT: 3 (Brainerd)

LIMITS:
Isanti-Kanabec County Line to JCT MN-23
Ref. Pt. 060+00.746 - 067+00.903


NOTES: CONTROL SECTION NOTES FROM SDW

Symbology:

Stick Map Legend				
Highway	State-Aid	Non State-Aid	City Limit	Bridge
			■ ■ ■ ■ ■ ■ ■ ■	◆

DISCLAIMER: If you encounter broken hyperlinks, please fill out Data Practice Form:

<http://www.dot.state.mn.us/information/datapractices/index.html>

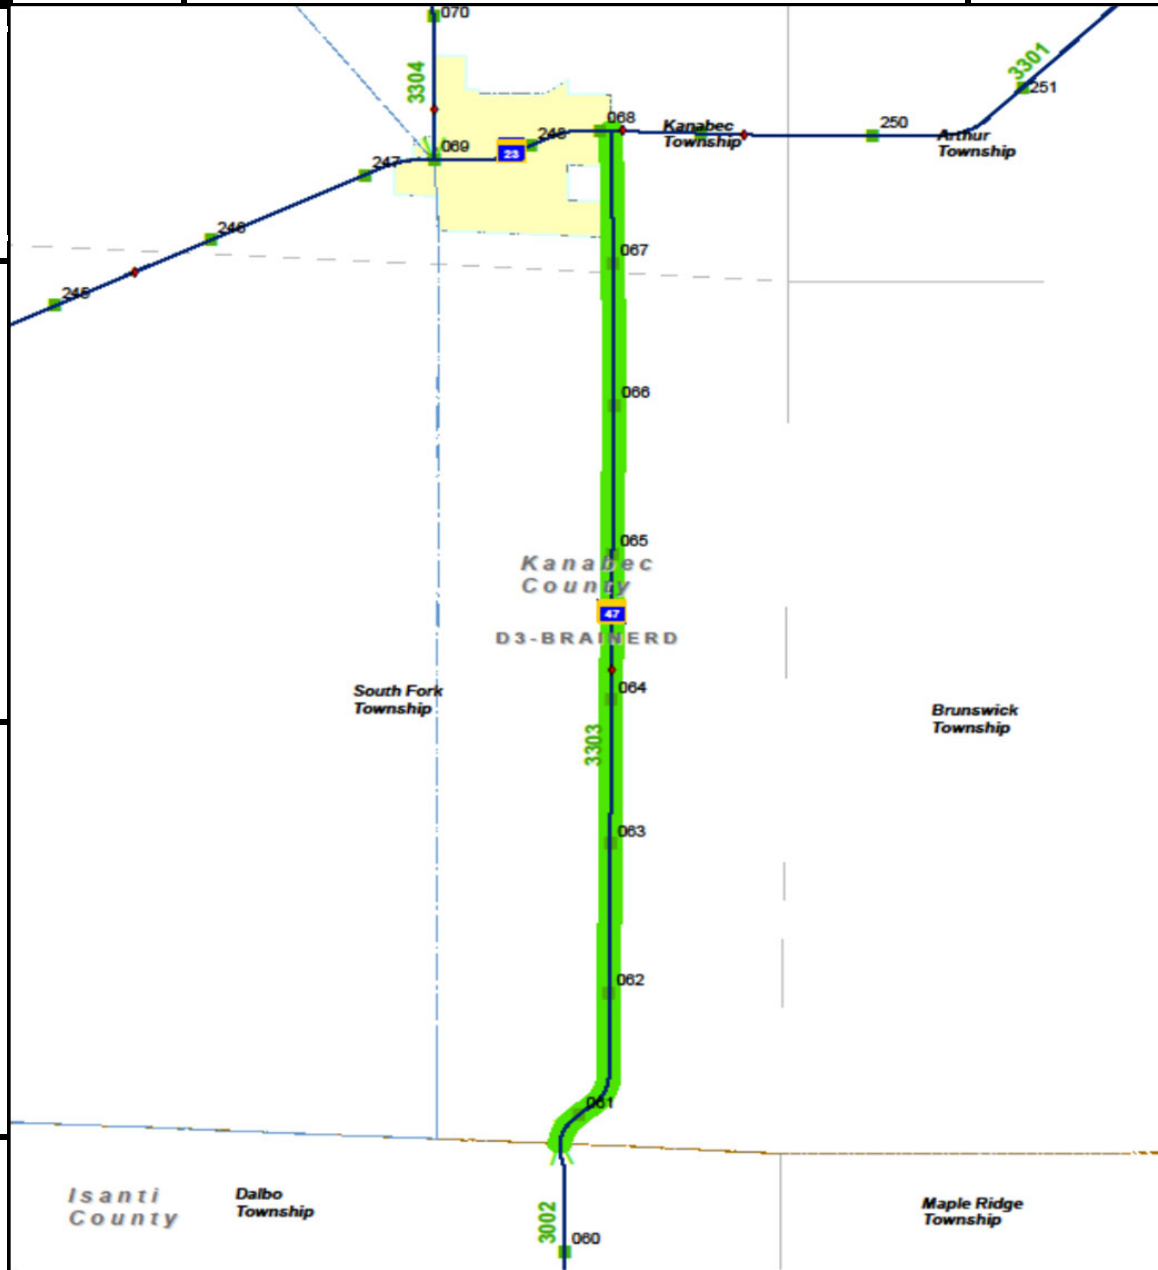


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 3303
TRUNK HIGHWAY 47
COUNTY Kanabec
DISTRICT 3B

LIMITS: S. Co. Line - E. Jct. T.H. 23 In Oglivie



YEAR BUILT	PROJECT N°	DESCRIPTION				CODE N°
		TYPE	WIDTH	THICK-NESS	REMARKS	
		Gravel Br. 745	18'	3/4"	No Record of Constr. Added in 1934. 60' B.S.	1
1923		Gravel	18'	3/4"	Co. Job 2303. 2304 & 2305. Added in 1934.	2
C 1944	A.F.E. 22 A.F.E. 6	Reshaping Grav. Surfacing	26'		608 C.Y. / Mi. Maint. Div.	3
M 1945	A.F.E. 6	Grav. Resurfacing	24'		783 C.Y. / Mi. Maint. Div.	4
C 1946	A.F.E. 21	Bit. Surfacing (Mixed Prime) Bit. Surf. Treat.	24'	3/4"	SC-3, 9786 Gal.	5
C 1947	A.F.E. 31	Sand-Grav. Lift Bit. Surf. Treat. (Mixed Prime)	26'	4"	SC-3, 103,093 Gal.	6
M 1948	A.F.E. 4	Spot Treat. Bit. Surf. Repair	26'		SC3, 5131 Gal. Agg. 398 Tons	7
C 1948	(1)	Br. 6672	30'		40' C.D.G.	8
M 1949	A.F.E. 4	Spot Treat. Bit. Surf. Repair	24'		SC3, 2814 Gal. Agg. 160 C.Y.	9
M 1950	A.F.E. 4	Spot Treat. Bit. Surf. Repair	24'		SC4, 6480 Gal. Agg. 400 C.Y.	10
C 1951	A.F.E. 19	Bit. Surfacing Mixed Bit.	24'	1"	SC-3, 53985 Gal. Agg. 4963 Tons	11
M 1954	A.F.E. 604	Bit. Surf. Repair	24'		SC4, 374 Gal. Agg. 39 Tons	12
M 1955	A.F.E. 604	Spot Treat. Bit. Surf. Repair	24'		SC-4, 8050 Gal. Agg. 735 Tons	13
M 1956	A.F.E. 818	Grade Correction & Restore Bit. Surf.	24'		SC-4, 2355 Gal. Bit. Mix 228 Tons	14

YEARS FROM	TOTAL MILES TO	UNINCORPORATED		INCORPORATED		RURAL		URBAN		
		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	
1934	1973	7.16	6.40	0.01	0.75	0.00	7.15	0.01	0.00	0.00
1974		7.16	6.65	0.01	0.50		7.15	0.01		

REMARKS: Layout is to scale as of 1934
(1) Built under Bridge Maintenance contract.

